CIV-Baseline Milestone01-05032026

ID	Task Name	Baseline Duration	Baseline Start	Baseline Finish	Duration	Actual Start	Actual Finish	% Comp.	Rem. Dur.
0	**Majorda Villa - Civil Works**	**101 days**	**20-02-26**	**18-06-26**	**99 days**	**20-02-26**	**NA**	**36%**	**62.93 days**
1	Start	0 days	20-02-26	20-02-26	0 days	20-02-26	20-02-26	100%	0 days
2	Mobilization at Site	1 day	20-02-26	20-02-26	1 day	20-02-26	20-02-26	100%	0 days
3	Surveying & Layout	1 day	21-02-26	21-02-26	1 day	21-02-26	21-02-26	100%	0 days
4	Approval for MEP - UGT, ST, SP	12 days	23-02-26	09-03-26	12 days	23-02-26	09-03-26	100%	0 days
5	Approval for Swimming Pool	12 days	23-02-26	09-03-26	12 days	23-02-26	09-03-26	100%	0 days
6	**Excavation**	**23 days**	**21-02-26**	**20-03-26**	**21 days**	**21-02-26**	**NA**	**84%**	**3.36 days**
7	Excavation in Foundation Pits	14 days	21-02-26	10-03-26	14 days	21-02-26	10-03-26	100%	0 days
8	Railing	2 days	10-03-26	11-03-26	2 days	10-03-26	11-03-26	100%	0 days
9	Rubble Soling	2 days	11-03-26	12-03-26	2 days	11-03-26	12-03-26	100%	0 days
10	PCC in Foundation	2 days	13-03-26	14-03-26	2 days	13-03-26	14-03-26	100%	0 days
11	Marking for Foundation	2 days	16-03-26	17-03-26	1 day	14-03-26	14-03-26	100%	0 days
12	Marking by Carpenter & Box Fitting	1 day	17-03-26	17-03-26	1 day	NA	NA	0%	1 day
13	Steel Tying Column Erection	2 days	18-03-26	19-03-26	2 days	NA	NA	0%	2 days
14	Steel Checking - Inspection Hold Po	1 day	20-03-26	20-03-26	1 day	NA	NA	0%	1 day
15	**Casting of Foundation**	**35 days**	**21-03-26**	**30-04-26**	**35 days**	**NA**	**NA**	**0%**	**35 days**
16	Starter for Column	2 days	21-03-26	23-03-26	2 days	NA	NA	0%	2 days
17	Casting for Column	1 day	23-03-26	23-03-26	1 day	NA	NA	0%	1 day
18	Column Shuttering & Casting - 1st S	3 days	24-03-26	26-03-26	3 days	NA	NA	0%	3 days
19	Column Shuttering & Casting - 2nd	4 days	27-03-26	31-03-26	4 days	NA	NA	0%	4 days
20	Excavation for Foundation Masonr	3 days	01-04-26	03-04-26	3 days	NA	NA	0%	3 days
21	Rubble Soling PCC in Foundation	2 days	04-04-26	06-04-26	2 days	NA	NA	0%	2 days
22	Foundation Masonry	5 days	07-04-26	11-04-26	5 days	NA	NA	0%	5 days
23	Backfilling in Plinth excavation for F	3 days	13-04-26	15-04-26	3 days	NA	NA	0%	3 days
24	Compaction for Plinth Pool Soling &	3 days	16-04-26	18-04-26	3 days	NA	NA	0%	3 days
25	Soling & PCC for Plinth Beam	1 day	20-04-26	20-04-26	1 day	NA	NA	0%	1 day
26	Steel for Plinth Beam	4 days	21-04-26	24-04-26	4 days	NA	NA	0%	4 days
27	Shuttering for Plinth Beam	5 days	25-04-26	30-04-26	5 days	NA	NA	0%	5 days
28	**Casting of Plinth Beam**	**8 days**	**01-05-26**	**09-05-26**	**8 days**	**NA**	**NA**	**0%**	**8 days**
29	Backfilling in Plinth	4 days	01-05-26	05-05-26	4 days	NA	NA	0%	4 days
30	Rubble Soling	4 days	06-05-26	09-05-26	4 days	NA	NA	0%	4 days
31	**PCC in Plinth**	**34 days**	**11-05-26**	**18-06-26**	**34 days**	**NA**	**NA**	**0%**	**34 days**
32	Column Steel & Starter	4 days	11-05-26	14-05-26	4 days	NA	NA	0%	4 days
33	Column Shuttering & Casting - 1st S	3 days	15-05-26	18-05-26	3 days	NA	NA	0%	3 days
34	Column Shuttering & Casting - 2nd Set with Staircase	3 days	19-05-26	21-05-26	3 days	NA	NA	0%	3 days
35	1F Slab Shuttering	10 days	22-05-26	02-06-26	10 days	NA	NA	0%	10 days
36	1F Steel tieing	9 days	03-06-26	12-06-26	9 days	NA	NA	0%	9 days
37	Side Shuttering & Electricals	3 days	13-06-26	16-06-26	3 days	NA	NA	0%	3 days

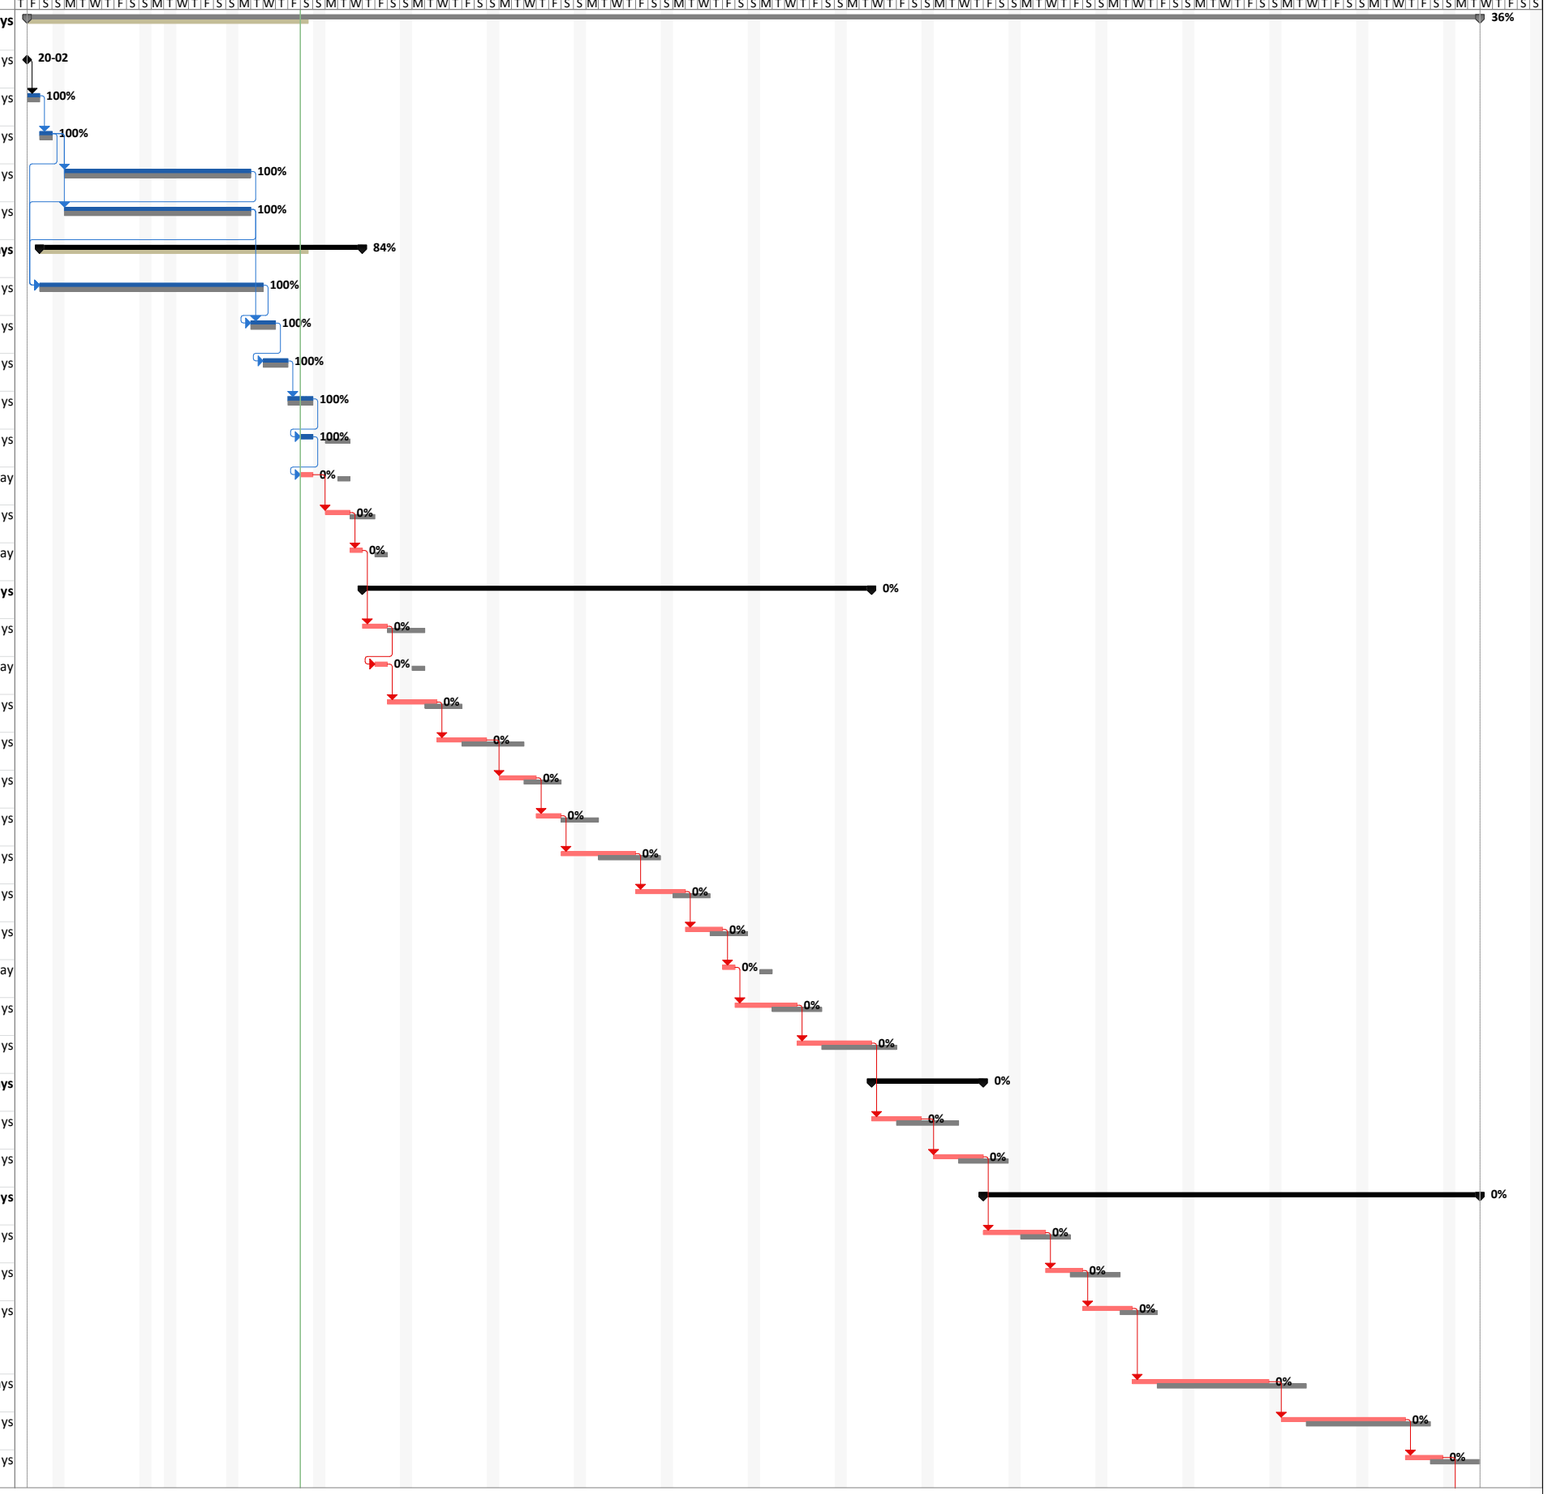

Critical | Critical Split | Critical Progress | Task | Split | Task Progress | Manual Task | Start-only | Finish-only | Duration-only | Baseline | Baseline Split | Baseline Milestone | Milestone | Summary Progress | Summary | Manual Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Deadline

CIV-Baseline Milestone01-05032026

ID	Task Name	Baseline Duration	Baseline Start	Baseline Finish	Duration	Actual Start	Actual Finish	% Comp.	Rem. Dur.
38	Casting for 1F Slab	2 days	17-06-26	18-06-26	2 days	NA	NA	0%	2 days
39	Completion of 1F Slab	0 days	18-06-26	18-06-26	0 days	NA	NA	0%	0 days



Critical		Task		Manual Task		Duration-only		Baseline Milestone		Summary		External Tasks		Inactive Milestone	
Critical Split		Split		Start-only		Baseline		Milestone		Manual Summary		External Milestone		Inactive Summary	
Critical Progress		Task Progress		Finish-only		Baseline Split		Summary Progress		Project Summary		Inactive Task		Deadline	
