FINAL-Majorda Project Plan

ID	Task Name	Baseline Duration	Baseline Start	Baseline Finish	Duration	Actual Start	Actual Finish	% Comp.	Finish Variance
0	**Majorda Villa - Civil Works**	**246 days**	**20-02-26**	**15-12-26**	**251 days**	**20-02-26**	**NA**	**18%**	**5 days**
1	Start	0 days	20-02-26	20-02-26	0 days	20-02-26	20-02-26	100%	0 days
2	Mobilization at Site	1 day	20-02-26	20-02-26	1 day	20-02-26	20-02-26	100%	0 days
3	Surveying & Layout	1 day	21-02-26	21-02-26	1 day	21-02-26	21-02-26	100%	0 days
4	Approval for MEP - UGT, ST, SP	12 days	23-02-26	09-03-26	12 days	23-02-26	09-03-26	100%	0 days
5	Approval for Swimming Pool	12 days	23-02-26	09-03-26	12 days	23-02-26	09-03-26	100%	0 days
6	Excavation in Foundation Pits	14 days	21-02-26	10-03-26	14 days	21-02-26	10-03-26	100%	0 days
7	Railing	2 days	10-03-26	11-03-26	2 days	10-03-26	11-03-26	100%	0 days
8	Rubble Soling	2 days	11-03-26	12-03-26	2 days	11-03-26	12-03-26	100%	0 days
9	PCC in Foundation	2 days	13-03-26	14-03-26	2 days	13-03-26	14-03-26	100%	0 days
10	Marking for Foundation	2 days	16-03-26	17-03-26	1 day	13-03-26	13-03-26	100%	-3 days
11	Marking by Carpenter & Box Fitting	1 day	17-03-26	17-03-26	1 day	14-03-26	14-03-26	100%	-2 days
12	Steel Tying Column Erection	2 days	18-03-26	19-03-26	7 days	17-03-26	24-03-26	100%	4 days
13	Steel Checking - Inspection Hold Point	1 day	20-03-26	20-03-26	1 day	25-03-26	25-03-26	100%	4 days
14	Casting of Foundation	1 day	21-03-26	21-03-26	1 day	27-03-26	27-03-26	100%	5 days
15	Starter for Column	1 day	23-03-26	23-03-26	1 day	NA	NA	0%	5 days
16	Casting for Column	1 day	23-03-26	23-03-26	1 day	NA	NA	0%	5 days
17	Column Shuttering & Casting - 1st Set	3 days	24-03-26	26-03-26	3 days	NA	NA	0%	5 days
18	Column Shuttering & Casting - 2nd Set	4 days	27-03-26	31-03-26	4 days	NA	NA	0%	5 days
19	Excavation for Foundation Masonry	3 days	01-04-26	03-04-26	3 days	NA	NA	0%	5 days
20	Rubble Soling PCC in Foundation	2 days	04-04-26	06-04-26	2 days	NA	NA	0%	5 days
21	Foundation Masonry	5 days	07-04-26	11-04-26	5 days	NA	NA	0%	5 days
22	Backfilling in Plinth excavation for Pool	3 days	13-04-26	15-04-26	3 days	NA	NA	0%	5 days
23	Compaction for Plinth Pool Soling & PCC	3 days	16-04-26	18-04-26	3 days	NA	NA	0%	5 days
24	Soling & PCC for Plinth Beam	1 day	20-04-26	20-04-26	1 day	NA	NA	0%	5 days
25	Steel for Plinth Beam	4 days	21-04-26	24-04-26	4 days	NA	NA	0%	5 days
26	Shuttering for Plinth Beam	5 days	25-04-26	30-04-26	5 days	NA	NA	0%	5 days
27	Casting of Plinth Beam	2 days	01-05-26	02-05-26	2 days	NA	NA	0%	5 days
28	Backfilling in Plinth	4 days	01-05-26	05-05-26	4 days	NA	NA	0%	5 days

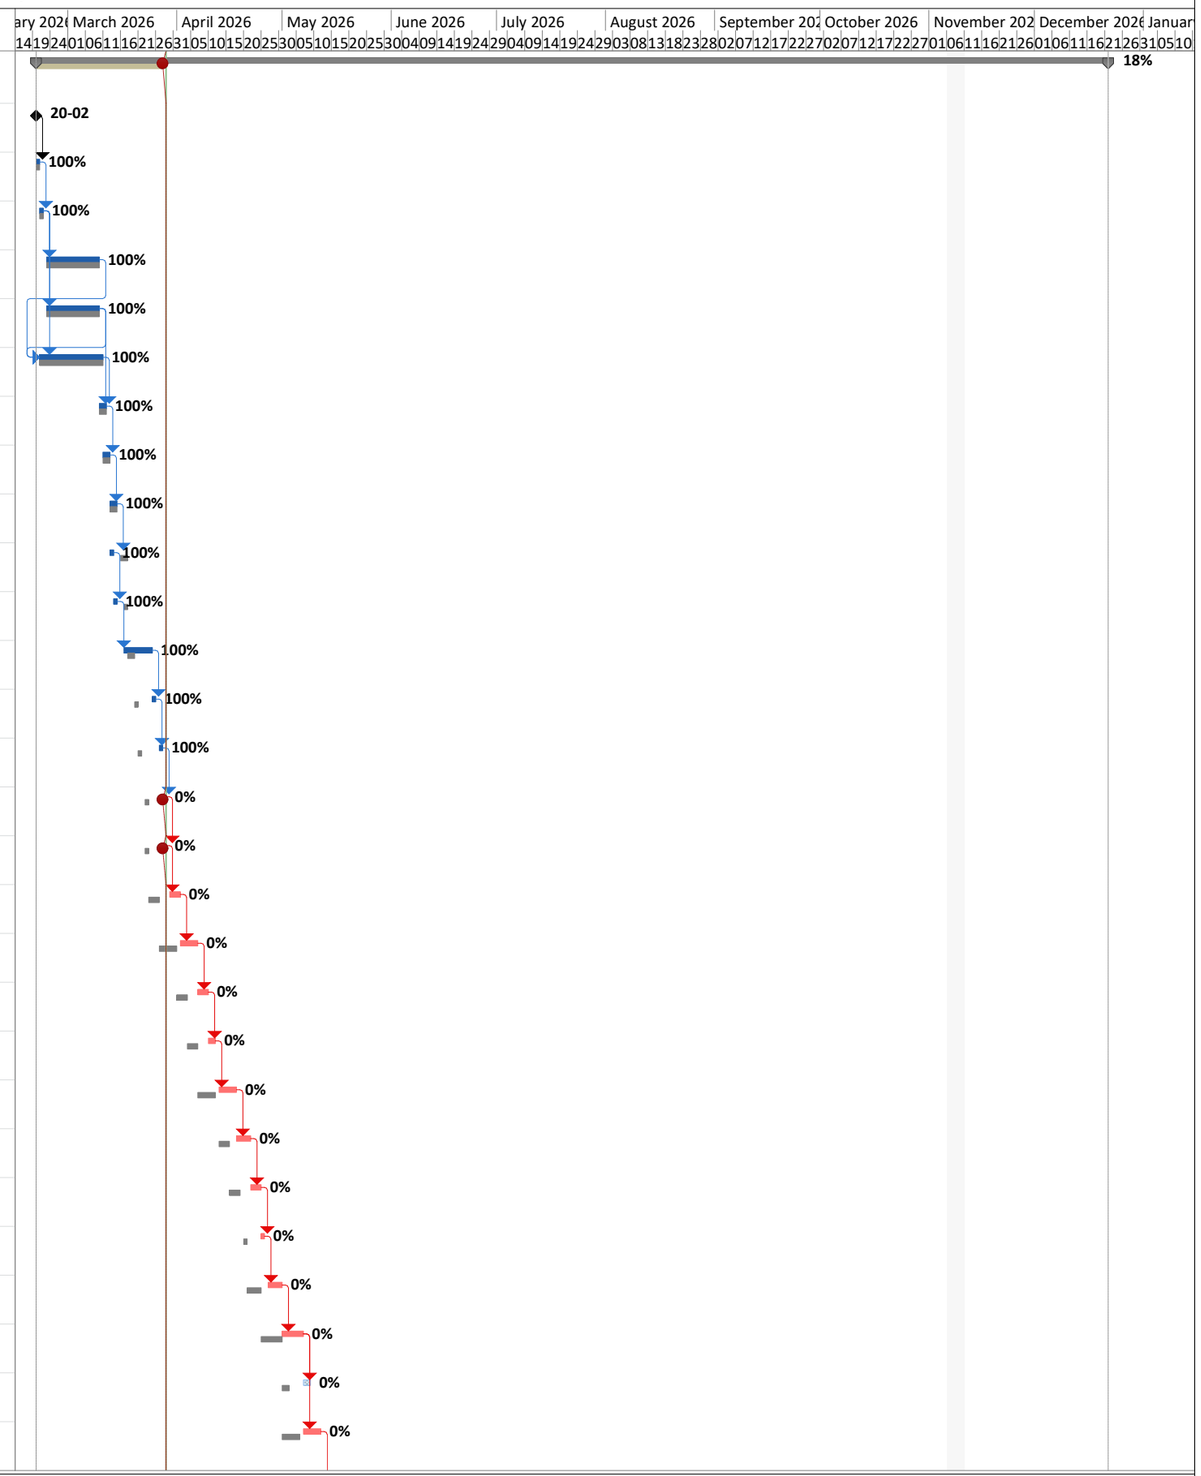

Critical | Split | Finish-only | Baseline Milestone | Manual Summary | Inactive Task
Critical Split | Task Progress | Duration-only | Milestone | Project Summary | Inactive Milestone
Critical Progress | Manual Task | Baseline | Summary Progress | External Tasks | Inactive Summary
Task | Start-only | Baseline Split | Summary | External Milestone | Deadline

FINAL-Majorda Project Plan

ID	Task Name	Baseline Duration	Baseline Start	Baseline Finish	Duration	Actual Start	Actual Finish	% Comp.	Finish Variance
29	Rubble Soling	4 days	06-05-26	09-05-26	4 days	NA	NA	0%	5 days
30	PCC in Plinth	2 days	11-05-26	12-05-26	2 days	NA	NA	0%	5 days
31	**Completion of Plinth (RA-01)**	0 days	12-05-26	12-05-26	0 days	NA	NA	0%	5 days
32	Column Steel & Starter	4 days	11-05-26	14-05-26	4 days	NA	NA	0%	5 days
33	Column Shuttering & Casting - 1st Set	3 days	15-05-26	18-05-26	3 days	NA	NA	0%	5 days
34	Column Shuttering & Casting - 2nd Set with	3 days	19-05-26	21-05-26	3 days	NA	NA	0%	5 days
35	1F Slab Shuttering	10 days	22-05-26	02-06-26	10 days	NA	NA	0%	5 days
36	1F Steel tieing	9 days	03-06-26	12-06-26	9 days	NA	NA	0%	5 days
37	Side Shuttering & Electricals	3 days	13-06-26	16-06-26	3 days	NA	NA	0%	5 days
38	Casting for 1F Slab	2 days	17-06-26	18-06-26	2 days	NA	NA	0%	5 days
39	**Completion of 1F Slab (RA-02)**	0 days	18-06-26	18-06-26	0 days	NA	NA	0%	5 days
40	**Completion of 2F Slab (RA-03)**	31 days	19-06-26	24-07-26	31 days	NA	NA	0%	5 days
41	**Completion of Masonry Works (RA-04)**	31 days	25-07-26	31-08-26	31 days	NA	NA	0%	5 days
42	**Completion of Internal Plastering (RA-05)**	49 days	01-09-26	30-10-26	49 days	NA	NA	0%	5 days
43	**Completion of External Plastering (RA-06)**	34 days	31-10-26	15-12-26	34 days	NA	NA	0%	5 days
44	**External Development & Final Bill (RA-07)**	34 days	31-10-26	15-12-26	34 days	NA	NA	0%	5 days

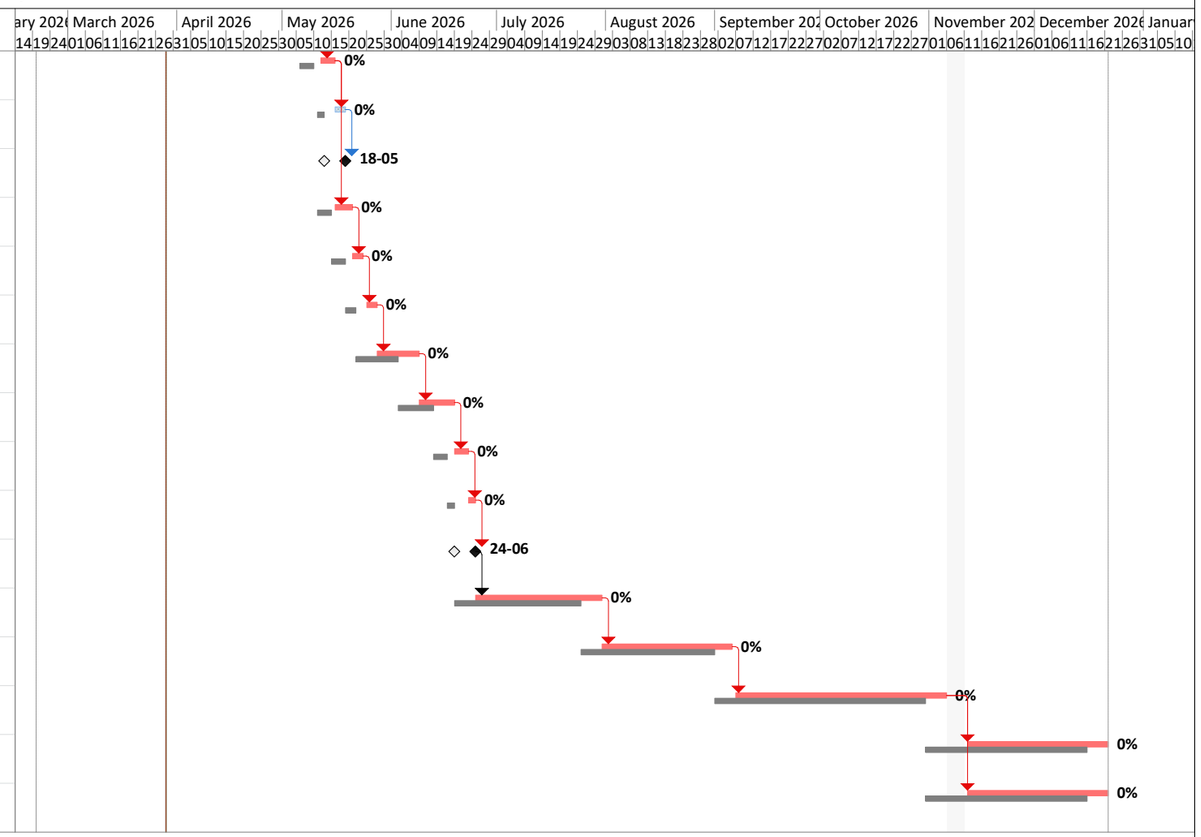

Critical		Split		Finish-only		Baseline Milestone		Manual Summary		Inactive Task	
Critical Split		Task Progress		Duration-only		Milestone		Project Summary		Inactive Milestone	
Critical Progress		Manual Task		Baseline		Summary Progress		External Tasks		Inactive Summary	
Task		Start-only		Baseline Split		Summary		External Milestone		Deadline	
