ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Cost
1		**Guirim Villament (BUA 1,704 Mtr2)**	**310 days**	**30-03-26**	**02-04-27**		**₹25,277,436.75**
2		Issuance of Mobilisation Advance	0 days	30-03-26	30-03-26		₹0.00
3		Site Mobilisation	10 days	30-03-26	09-04-26	2	₹0.00
4		Excavation	15 days	10-04-26	27-04-26	3	₹0.00
5		Raft Foundation	20 days	28-04-26	20-05-26	4	₹0.00
6		**RCC Works**	**150 days**	**21-05-26**	**16-11-26**		**₹0.00**
7		GF Slab	30 days	21-05-26	24-06-26	5	₹0.00
8		First Floor Slab	30 days	25-06-26	29-07-26	7	₹0.00
9		Second Floor Slab	30 days	30-07-26	03-09-26	8	₹0.00
10		Third Floor Slab	30 days	04-09-26	12-10-26	9	₹0.00
11		Fourth Floor Slab	30 days	13-10-26	16-11-26	10	₹0.00
12		**Masonry Works**	**125 days**	**30-07-26**	**29-12-26**		**₹0.00**
13		Ground Floor	25 days	30-07-26	28-08-26	8	₹0.00
14		First Floor	25 days	29-08-26	30-09-26	13	₹0.00
15		Second Floor	25 days	01-10-26	29-10-26	14	₹0.00
16		Third Floor	25 days	30-10-26	27-11-26	15	₹0.00
17		Fourth Floor	25 days	28-11-26	29-12-26	16	₹0.00
18		**Plastering Works**	**125 days**	**01-10-26**	**26-02-27**		**₹0.00**
19		Ground Floor	20 days	01-10-26	23-10-26	14	₹0.00
20		First Floor	20 days	24-10-26	16-11-26	19	₹0.00
21		Second Floor	20 days	17-11-26	09-12-26	20	₹0.00
22		Third Floor	20 days	10-12-26	05-01-27	21	₹0.00
23		Fourth Floor	20 days	06-01-27	28-01-27	22	₹0.00
24		External Plaster	45 days	06-01-27	26-02-27	22	₹0.00
25		MEP Work	30 days	27-02-27	02-04-27	24	₹0.00
26		Site Development	30 days	27-02-27	02-04-27	24	₹0.00
27		Civil Works Hand Over	0 days	02-04-27	**02-04-27**	26	₹0.00
28		**Payment Schedule**	**235 days**	**20-05-26**	**26-02-27**		**₹25,277,436.75**
29		Plinth Completion	0 days	20-05-26	20-05-26	5	₹3,600,000.00
30		Ground Floor Slab	0 days	24-06-26	24-06-26	7	₹3,600,000.00
31		First Floor Slab + Ground Floor Masonry	0 days	28-08-26	28-08-26	8,13	₹3,600,000.00
32		Second Floor Slab + First Floor Masonry	0 days	16-11-26	16-11-26	15,20	₹3,600,000.00
33		Third Floor Slab + Second Floor Masonry	0 days	09-12-26	09-12-26	16,21	₹3,600,000.00
34		Forth Floor Slab + Third Floor Masonry	0 days	05-01-27	05-01-27	17,22	₹3,600,000.00
35		Plastering Complete (Internal + External)	0 days	26-02-27	26-02-27	24	₹3,677,436.75

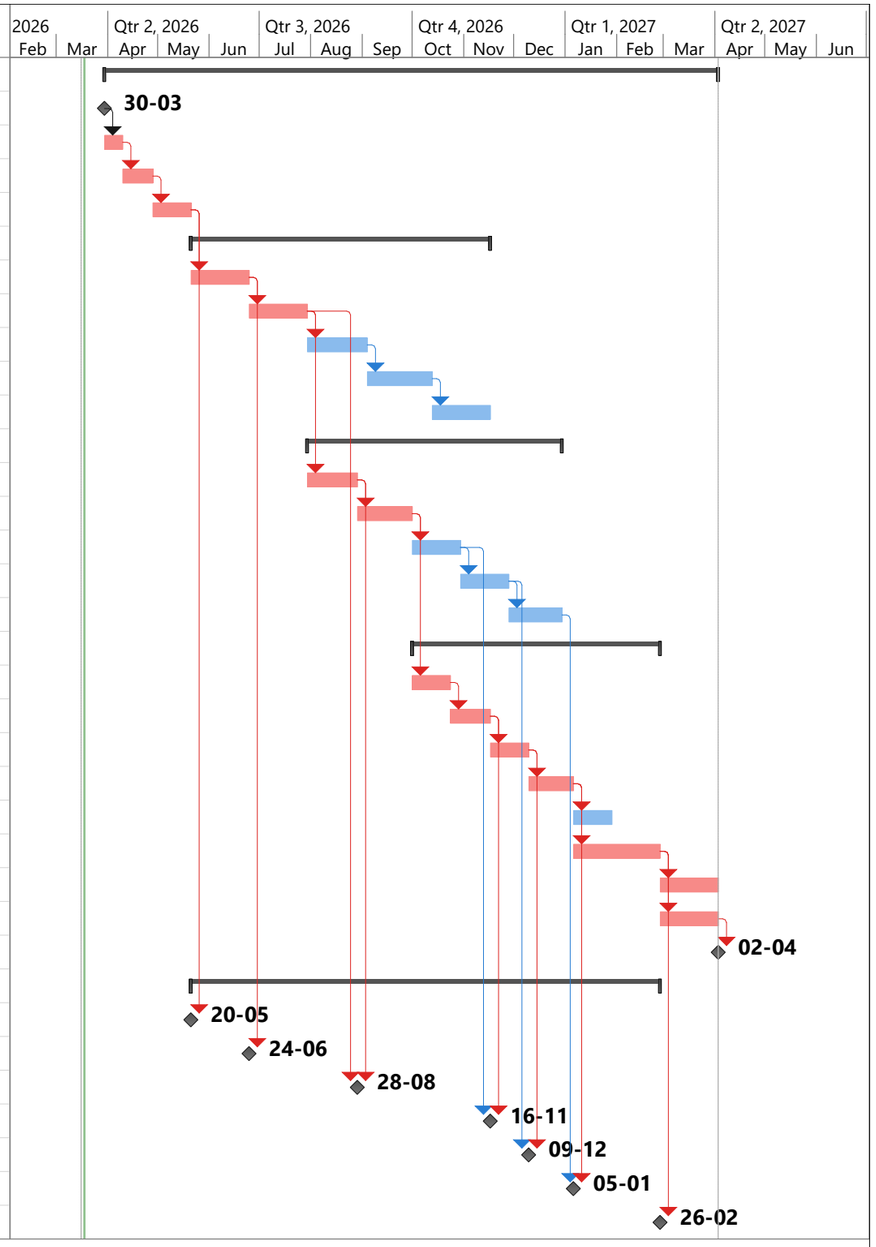

Project: Guirim Villament
Date: 18-03-26

Task	Inactive Task	Manual Summary Rollup	External Milestone	Manual Progress
Split	Inactive Milestone	Manual Summary	Deadline	
Milestone	Inactive Summary	Start-only	Critical	
Summary	Manual Task	Finish-only	Critical Split	
Project Summary	Duration-only	External Tasks	Progress	
